S CURVE

Sl. No	Activity	Jan-19	Feb-19	Mar-19	Apr-19	May-19	Jun-19	Jul-19	Aug-19	Sep-19	Oct-19	Nov-19	Dec-19	Jan-20	Feb-20	Mar-20	Apr-20	May-20	Jun-20
1	Earthwork																		
2	GSB																		
3	WMM																		
4	DBM																		
5	BC																		
6	BM																		
7	Hard shoulder																		
8	Pipe Culvert																		
9	Slab Culvert																		
10	Minor Bridge																		
11	Major Bridge																		
12	Traffic Sigs & Other Appurtenances																		
13	Km. STONES, BOUNDARY STONE, ETC.																		
14	Concrete work																		
15	Bus Bay																		
16	Miscellaneous (Site clearance, Quality Control,Crust removal/																		
17	Road side plantation																		
17	Toe wall /retaining wall																		

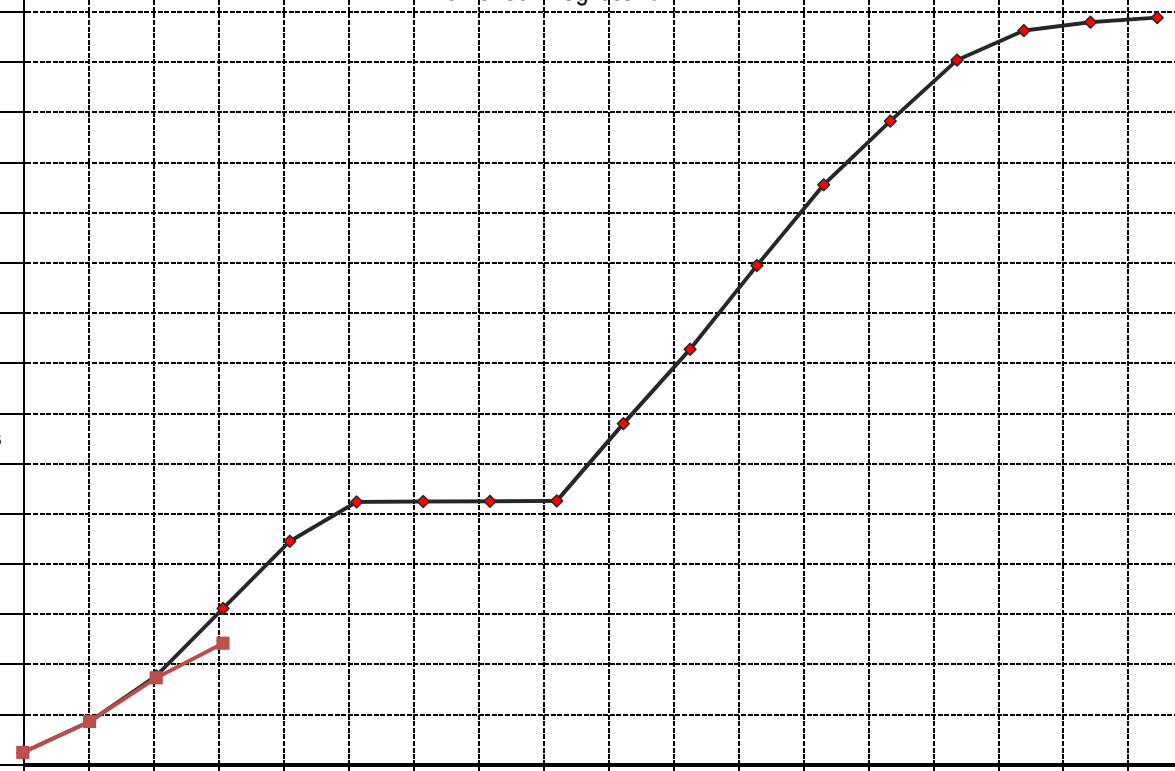

		Jan-19	Feb-19	Mar-19	Apr-19	May-19	Jun-19	Jul-19	Aug-19	Sep-19	Oct-19	Nov-19	Dec-19	Jan-20	Feb-20	Mar-20	Apr-20	May-20	Jun-20
Planned Progress (%)	Monthly	0.49%	4.18%	6.20%	9.12%	9.12%	5.31%	0.05%	0.05%	0.05%	10.46%	10.06%	11.36%	10.92%	8.62%	8.28%	3.97%	1.14%	0.63%
	Cummul.	0.49%	4.67%	10.87%	19.98%	29.10%	34.41%	34.46%	34.51%	34.56%	45.02%	55.08%	66.44%	77.36%	85.97%	94.26%	98.23%	99.37%	100.00%
Achieved Progress (%)	Monthly	0.49%	4.18%	5.92%	4.69%														
	Cummul.	0.49%	4.67%	10.59%	15.28%														

CONCESSIONAIRE **INDEPENDENT ENGINEER**
